

Lot: 41 (Existing)
S. I., N. Y.



Soil Percolation Test

Scale: 1" = 20'-0"


Drawing # 1 of 2



Gaspere Rosário Santoro
M.S.C.E., P.E., P.P.
Consulting Engineer/Planner

11 Brick Court, Unit #5
Staten Island, NY 10309
(718) 356-3826
F: (718) 356-3853

DRYWELL PERCOLATION TEST

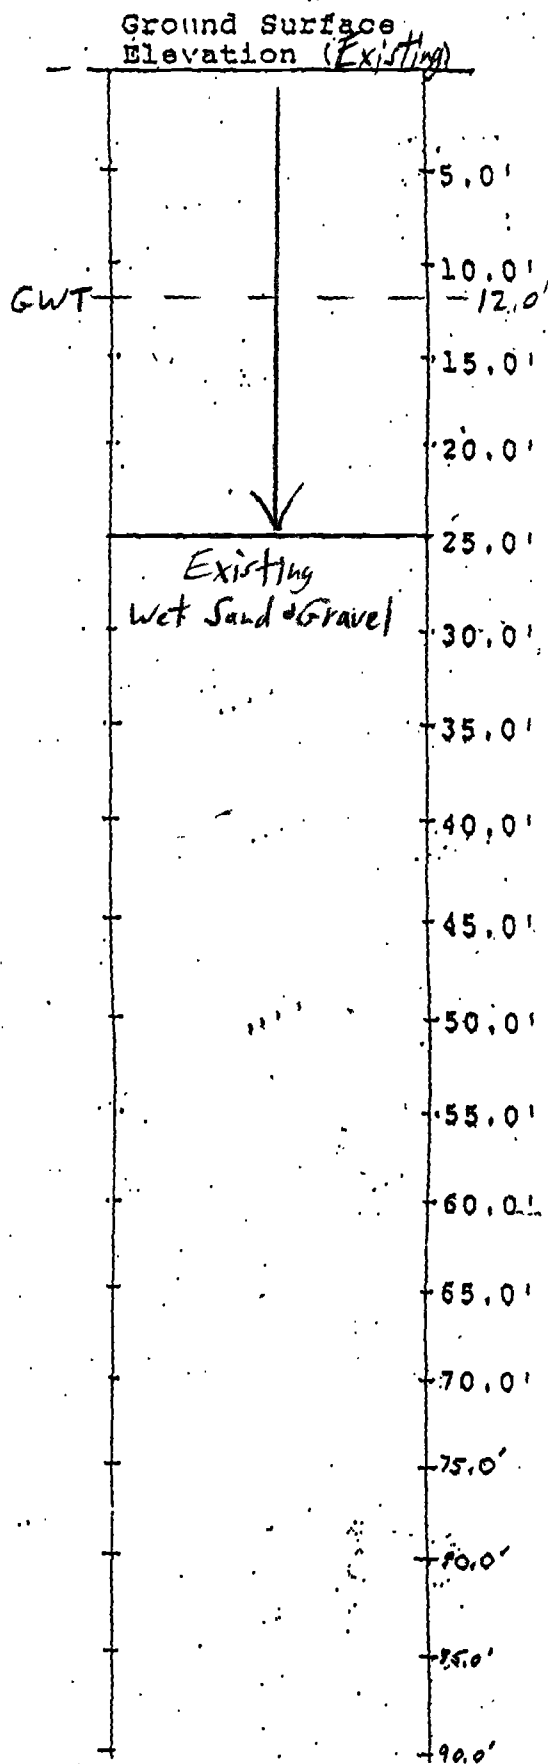

6" Ø TEST HOLE FILLED

WITH WATER

COMPLIED WITH RS16, P113

Drywell Percolation Test per Local law 103/89 & RS-16.

LOCATION: Moreland St.

BLOCK: 3820 LOT: 41 (Existing)

APPLICATION NUMBER:

PERCOLATION TEST CONDUCTED ON: 4/9/15

Test Hole 6" Ø Dug to a Depth of 23 feet. Hole filled with WATER
RS16, P113

Ground Water Encountered @ 12'

System Saturated with Water. Steady Percolation Rate Achieved After Saturation is: 3.10 Gallons per min.

NOTE: Elevations refer to Borough of Staten Island Datum, which is 3.19' above Sandy Hook, N.J. established by U.S.G.S.


DRAWING # 2 OF 2 DRAWINGS

Section Through Test Hole Vertical
Scale: 1" = 10.00'

TEST HOLE 1

Gaspere Rosário Santoro
M.S.C.E., P.E., P.P.
Consulting Engineer/Planner

11 Brick Court, Unit #5
Staten Island, NY 10309



NOTE: Ground water table can appear/ fluctuate due to rain, tides and cresting ground water on dates other than signed herewith.
